Citizens'
Oversight
Committee

Bond Program Update

May 22, 2023




FREMONT UNION
HIGH SCHOOL DISTRICT



Agenda

- 1. Big Ten Projects and Bond Project Schedule
- 2. FHS Science Building Modernization
- 3. FHS New Field House and Athletic Complex
- 4. MVHS Building F3 Choir Modernization
- 5. HHS Science Building Modernization
- 6. HHS Building B Classroom Modernization and Seismic Upgrades
- 7. HHS Library Quad Improvements
- 8. CHS Buildings 200 & 700 Modernization
- 9. LHS New Science Building
- 10. LHS Voyager Building
- 11. Maintenance and Operations Building
- 12. Adult Ed Classrooms and District Office Parking Lot/Solar Panels
- 13. District Robotics Center
- 14. Sunnyvale Lakewood Library
- 15. Bond Issuance and Financial Update

FUHSD Bond Projects



Maintenance & Operations Building

LHS New Science Building

MVHS Bldg F3 Choir Modernization

FHS Science Building Modernization


HHS Science Building Modernization

CHS Building 200 and 700 Modernization

Adult School Classroom Modernization and DO Parking Lot/Solar Panels

LHS New Voyager Building

FHS New Field House and Athletic Complex

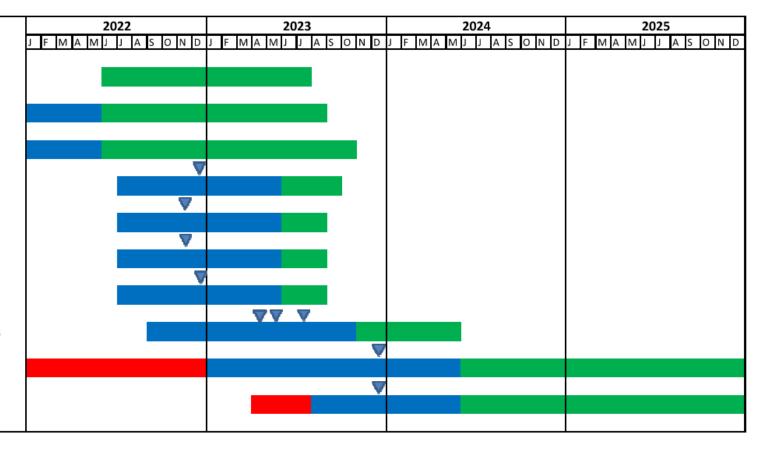






FHS Science Building Modernization

- Designer: Derivi Castellanos Architects (DCA)
- Design Status: DSA Approved
- Preconstruction Status: Submittals and Procurement
- Construction Schedule: June August 2023
- Occupancy (Anticipated): August 2023
- Contractor: Beals Martin
- Increased Scope:
 - Added Exterior Improvements (New Tiles)
 - Additional ADA Upgrades

FHS Science Building Modernization

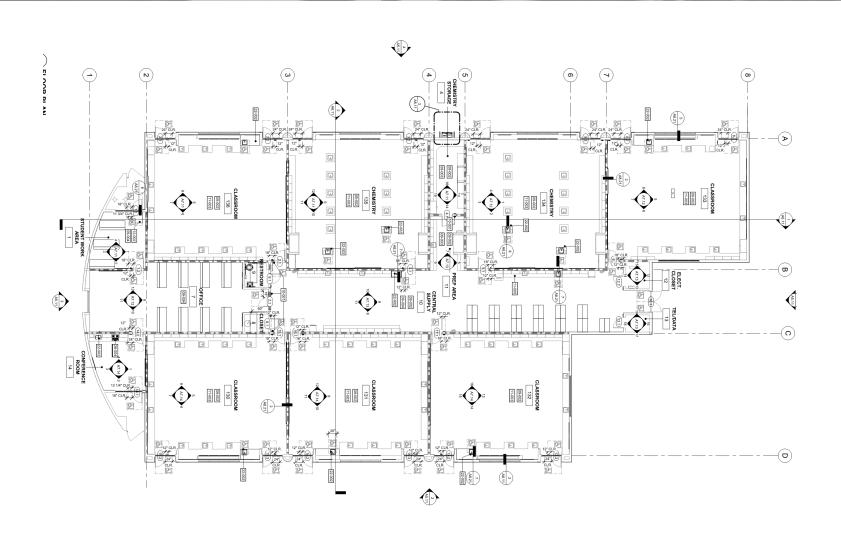

FHS New Field House and Athletic Complex

- Designer: Aedis Architects
- Design Status:
 Programming and Master
 Plan Review
- Anticipated Construction
 Schedule: Fall 2024 Fall 2025








FREMONT UNION
HIGH SCHOOL DISTRICT




MVHS Building F3 Modernization

- Designer: Derivi Castellanos Architects (DCA)
- Design Status: DSA Approved
- Preconstruction Status: Submittals and Procurement
- Construction Schedule: June September 2023
- Occupancy (Anticipated): October 2023
- Contractor: Lathrop Construction
- Increased Scope:
 - Added Practice Rooms
 - Custom Audio Visual (AV) System
 - Increased Building square footage
 - Additional storage
 - Significant ADA Upgrades

MVHS Building F3 Modernization

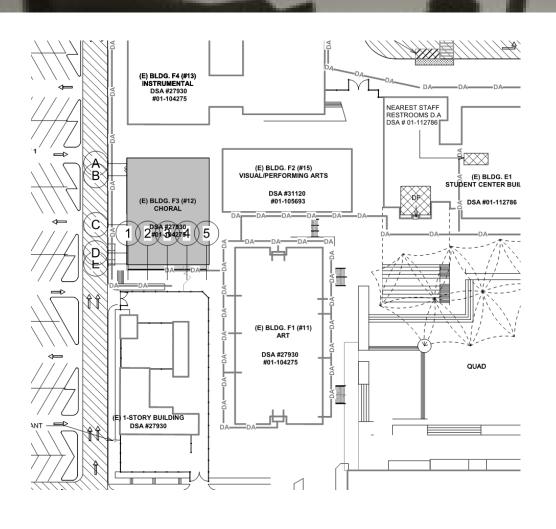

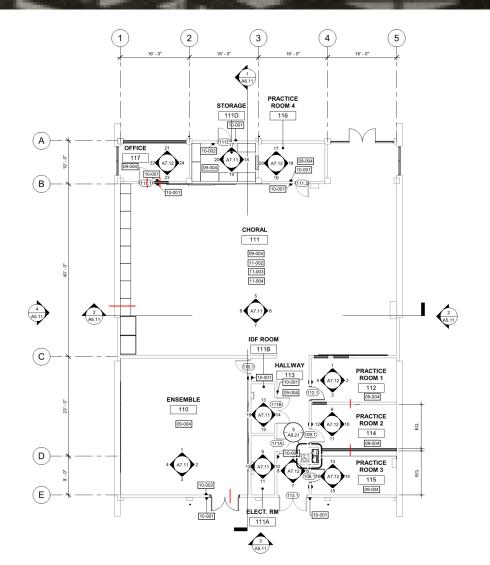




HHS Science Building Modernization


- Designer: Quattrocchi Kwok Architects (QKA)
- Design Status: DSA Approved
- Preconstruction Status: Submittals and Procurement
- Construction Schedule: June August 2023
- Occupancy (Anticipated): August 2023
- Contractor: Lathrop Construction
- Increased Scope:
 - New Building Envelope System
 - Extensive ADA Upgrades
 - Additional Custodial Closet

HHS Science Building Modernization

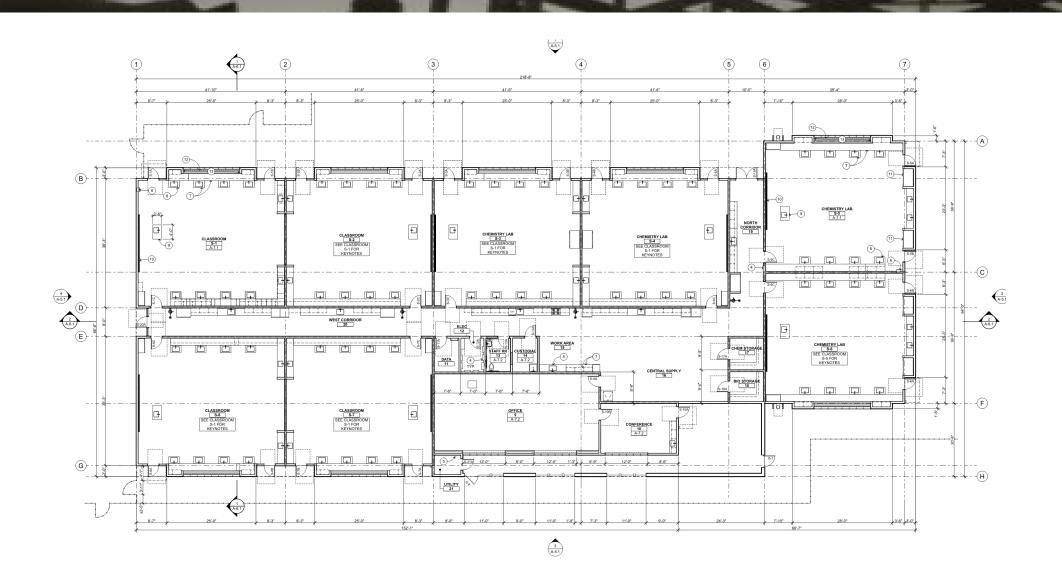

HHS Building B Classroom Modernization and Seismic Upgrades Project


- Designer: Quattrocchi Kwok Architects (QKA)
- Construction Status: Bldg. B near completion. Site work in progress
- Construction Schedule: June 2022 August 2023
- Occupancy (Anticipated): Summer 2023
- Contractor: Blach Construction Company

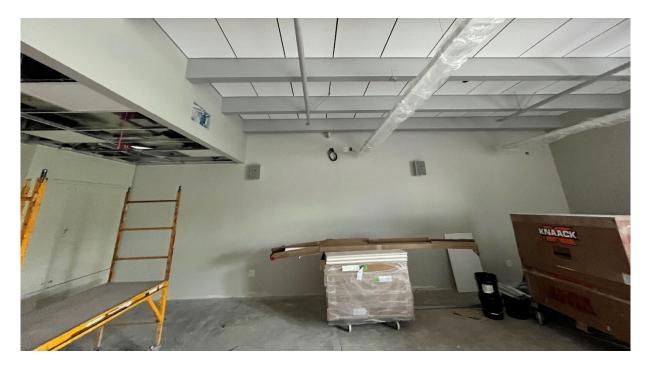










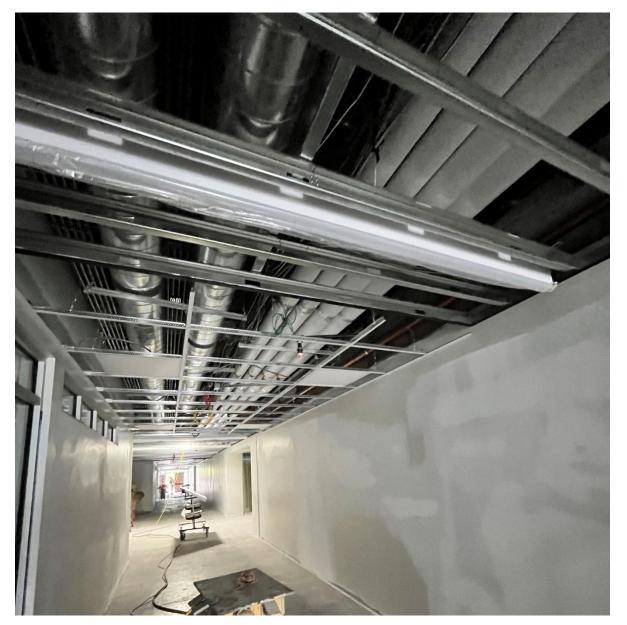

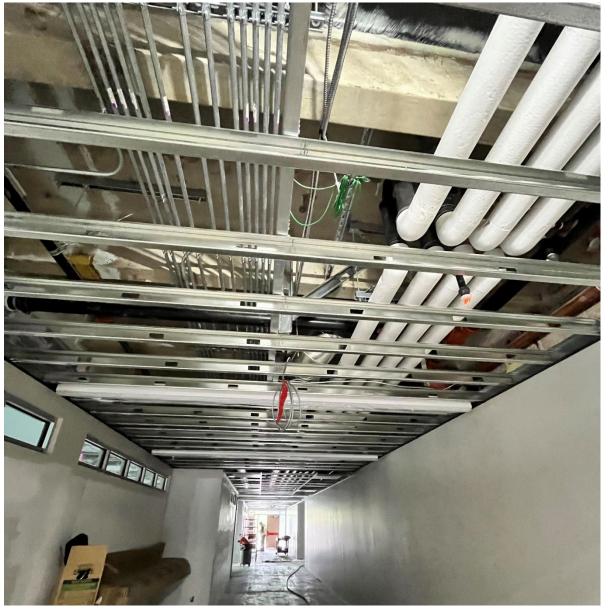

HHS Library Quad Improvements

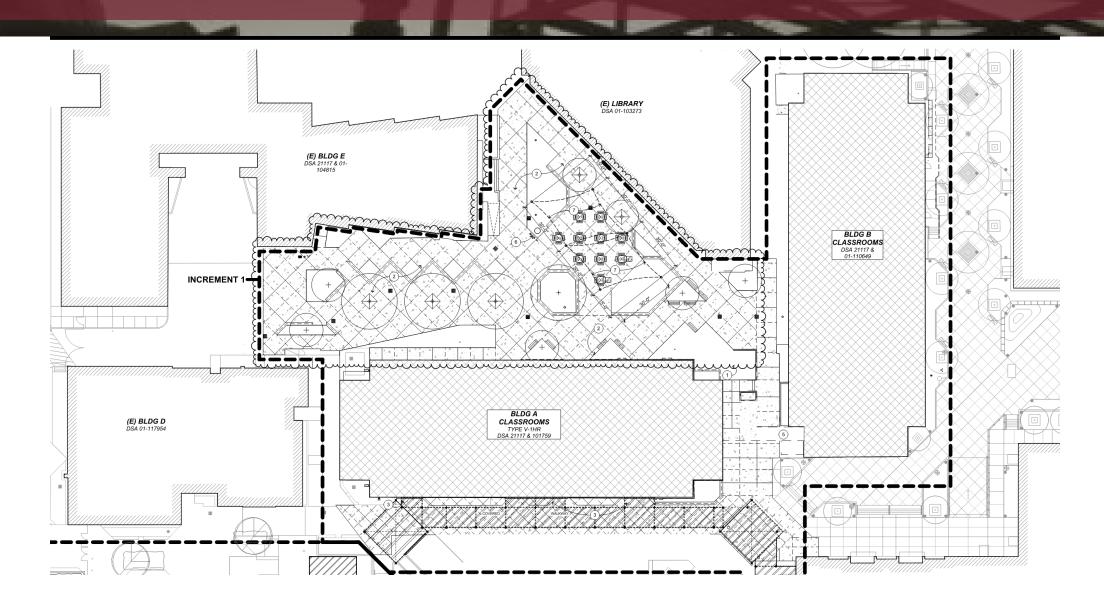

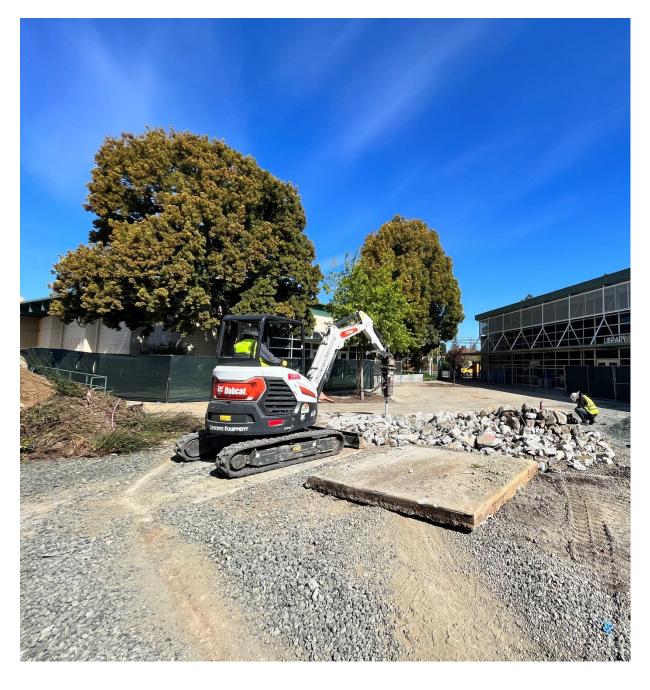










FREMONT UNION
HIGH SCHOOL DISTRICT




CHS Buildings 200 and 700 Modernization

- Designer: McKim Design Group
- Design Status: DSA Approved
- Preconstruction Status: Submittals and Procurement
- Construction Schedule: June August 2023
- Occupancy (Anticipated): August 2023
- Contractor: Blach Construction Company


Building 200 Floor Plan

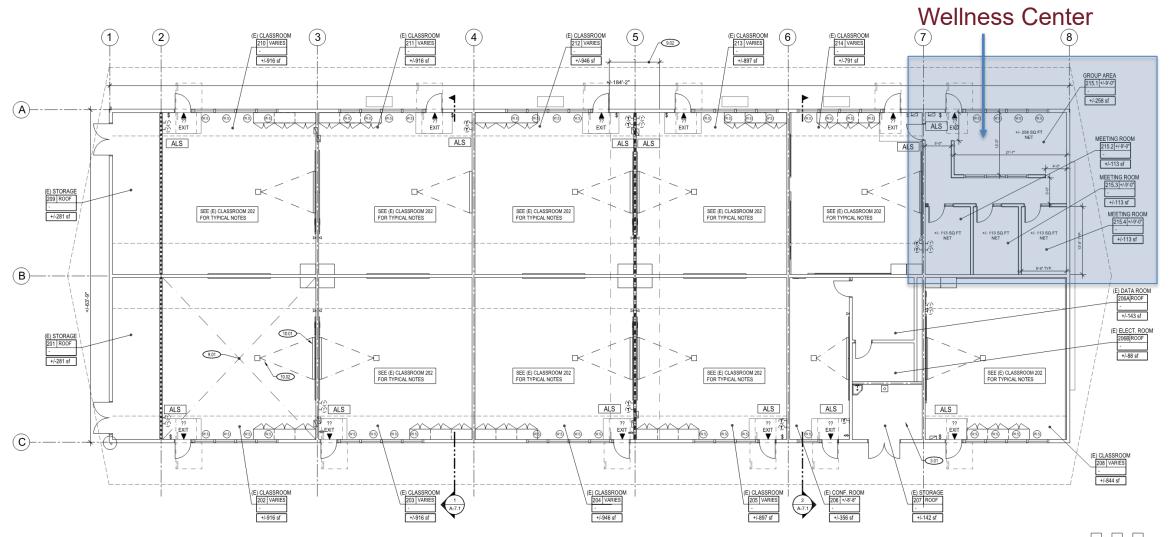






CHS Building 200 – Wellness Center

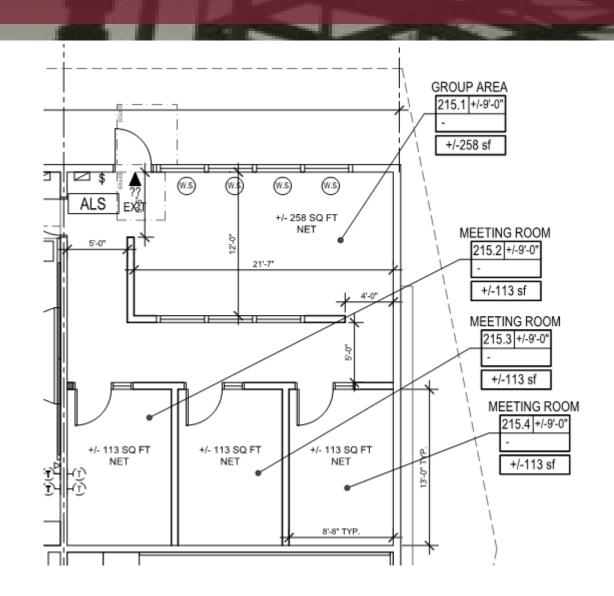


Building 700 Floor Plan

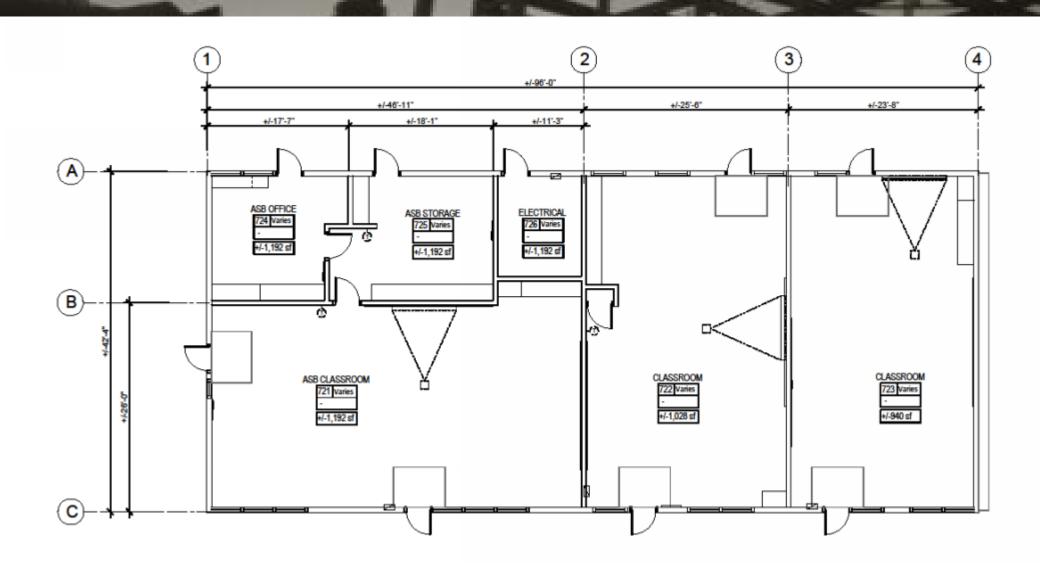




LHS New Science Building

- Designer: Quattrocchi Kwok Architects (QKA)
- Construction Status: Mechanical, electrical and plumbing rough-in, lath and plaster
- Construction Schedule:
 - Increment 1 Site Package: June 2022 September 2022
 - Increment 2 New Building: October 2022 November 2023
- Occupancy (Anticipated): Fall 2023
- Contractor: Blach Construction Company

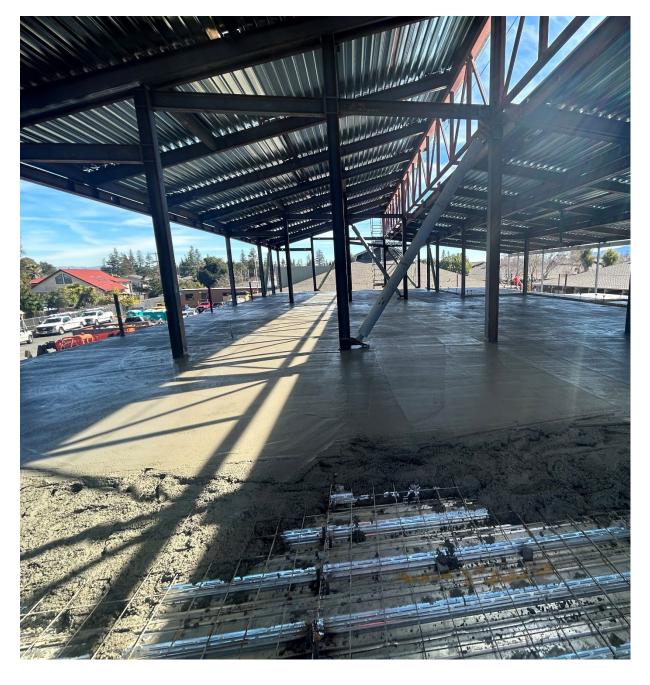





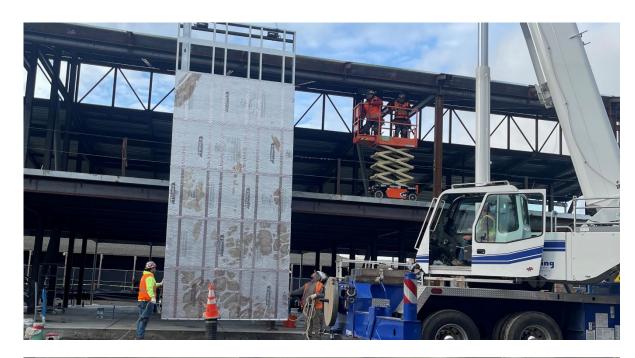




























LHS Voyager Building


- Designer: Quattrocchi Kwok Architects (QKA)
- Design Status: Schematic Design
- Anticipated Construction
 Schedule: June 2024 August
 2025

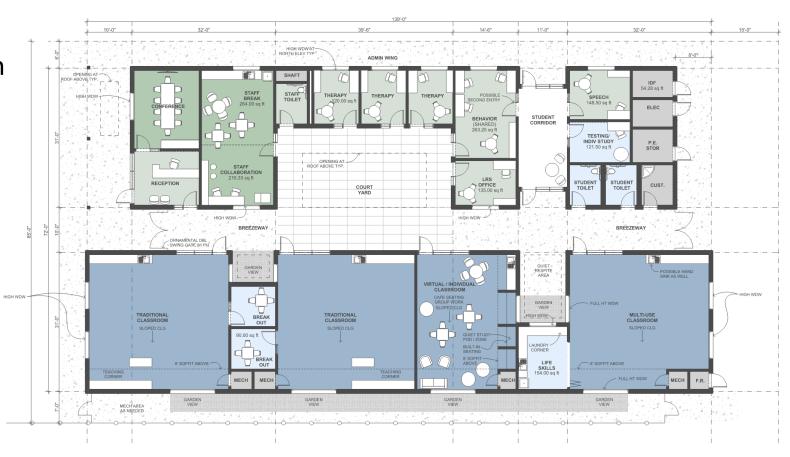



District Office Maintenance and Operations Building

- Designer: Quattrocchi Kwok Architects (QKA)
- Construction Status: Interior finishes, lath and plaster
- Construction Schedule: June 2022 September 2023
- Occupancy (Anticipated): Fall 2023
- Contractor: Blach Construction Company

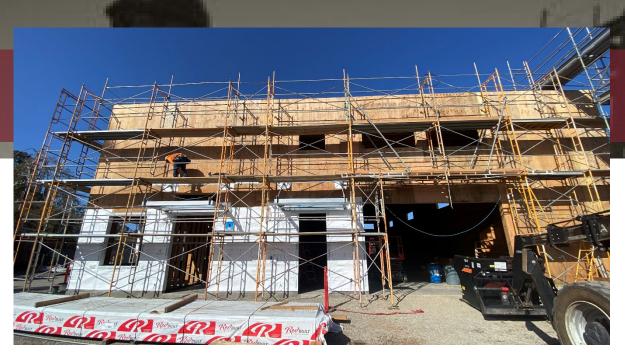





















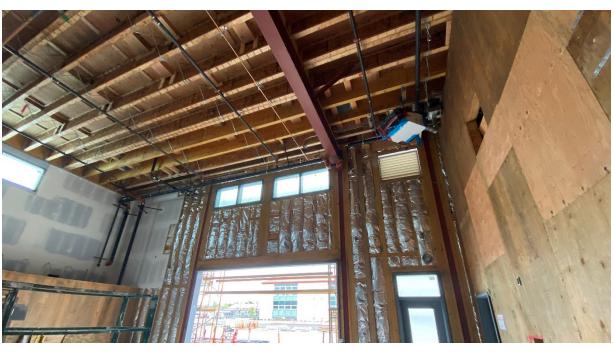


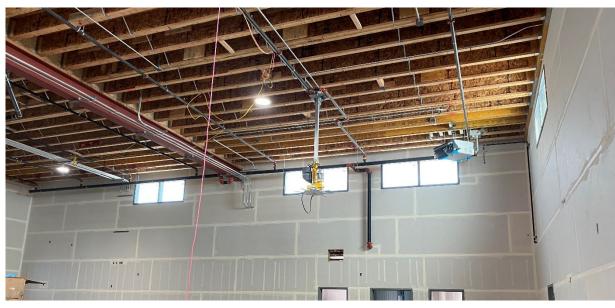




Adult Education Classroom Modernization

- Designer: Quattrocchi Kwok Architects (QKA)
- Design Status: DSA Submittal
- Anticipated Construction Schedule: Fall 2023 Spring 2024
- Contractor: Blach Construction Company

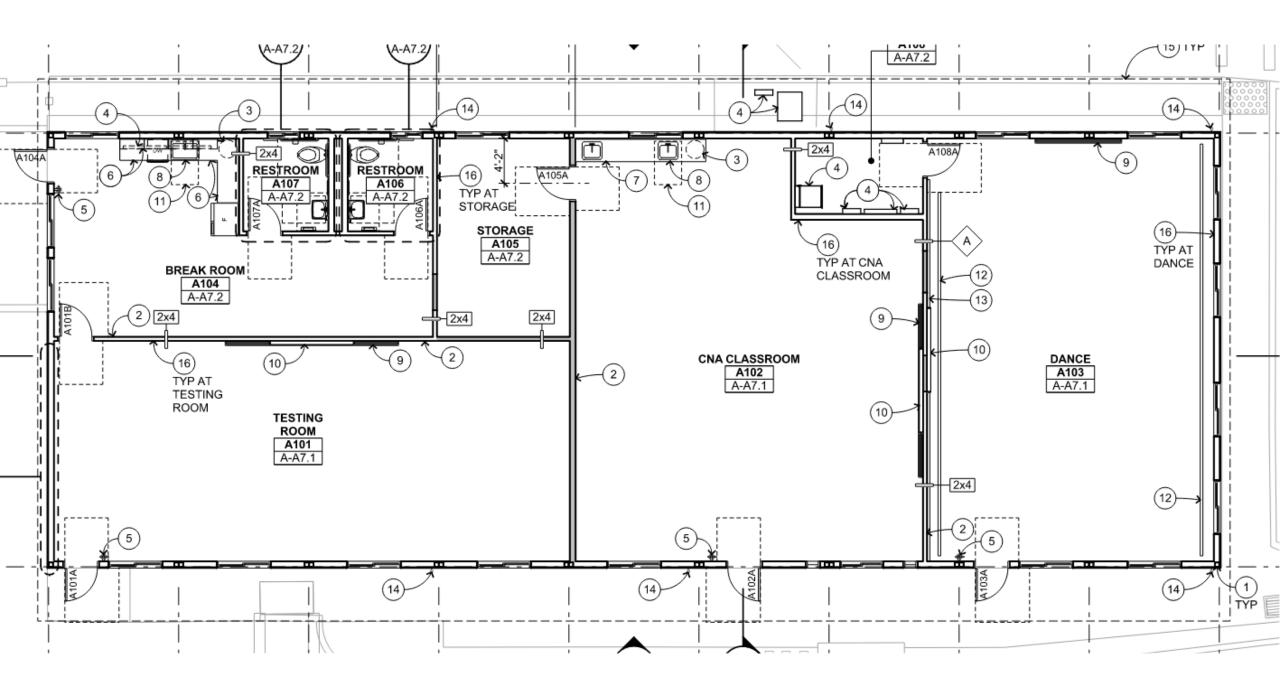

District Office Parking Lot and Solar Canopies


- Designer: Quattrocchi Kwok Architects (QKA)
- Design Status:
 - Increment 1 Parking Lot: DSA Submittal
 - Increment 2 Solar Canopies: Design Development
- Anticipated Construction Schedule: Fall 2023 Spring 2024
- Contractor: Blach Construction Company

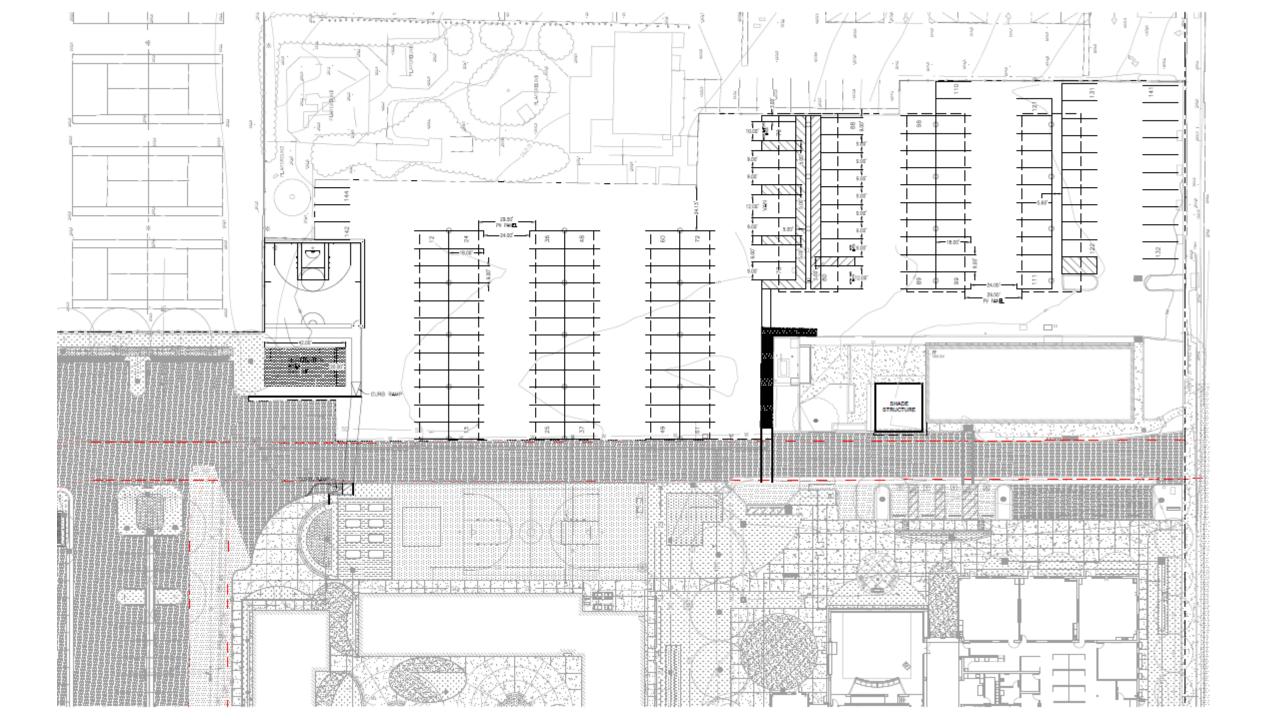

District Robotics Center

- Designer: Quattrocchi Kwok Architects (QKA)
- Design Status: Programming and Site Feasibility
- Anticipated Construction Schedule: Fall 2024 – Fall 2025


PROGRAM ADJACENCIES

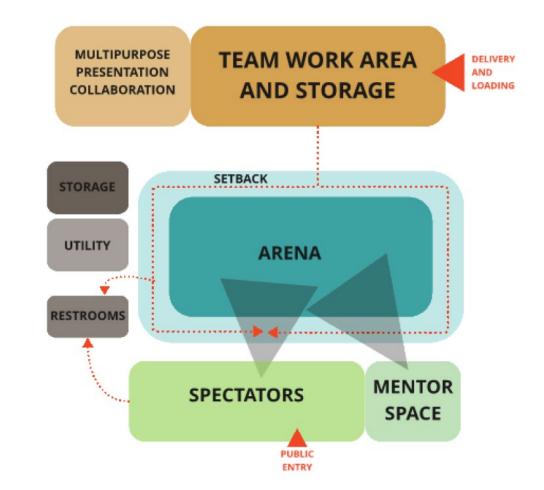

District Robotics Center

CUPERTINO SITE PLAN



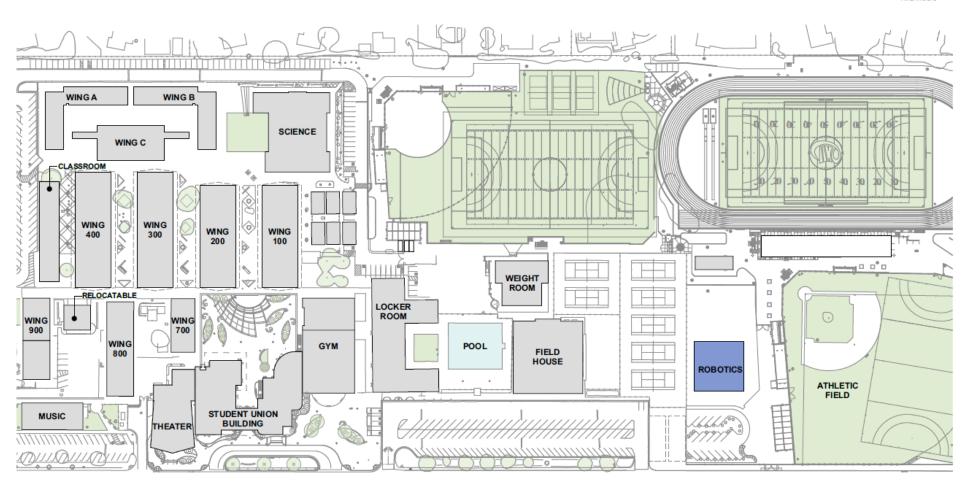





FREMONT UNION
HIGH SCHOOL DISTRICT



Sunnyvale Lakewood Library Project



Sunnyvale Lakewood Library Project



Sunnyvale Lakewood Library Project

Joint MOU Approved (3 Party)

Winter 2020

City of Sunnyvale

Fremont Union High School District

Sunnyvale School District

Schematic Design Approval

DSA Submittal

DSA Approval

Bidding

Start Construction

Completion

November 2020

October 2022

Spring 2023

Summer 2023

Fall 2023

End of 2024





FREMONT UNION
HIGH SCHOOL DISTRICT



Bond Issuance, Series 2023

The Series 2023 bonds will have the following characteristics:

- Not-to-exceed par amount of \$210 million.
 - √ \$110 million from 2018 Measure
 CC authorization (last issuance)
 - ✓ \$100 million from 2022 MeasureG authorization (first issuance)
 - ✓ Par amount was determined based on projected capital facility needs over the next two to three years.
- Refunding Bonds component, conservatively estimated to save taxpayers over \$1 million.

Key Dates	
Board Study Session	April 4
Meeting Rating Agency	Week of April 10
District Board Meeting	May 2
Receive Rating	May 5
County Board Meeting	May 16
Print and Mail POS	May 17
Price Bonds	May 24
Closing	June 7

Bond Issuance, Series 2023

FUHSD Receives 'Aaa' and 'AAA' credit ratings from Moody's and Standard & Poor's ("S&P"), respectively

Highest Possible credit ratings available to School Districts and are attributed to:

- Robust financial position supported by strong operating performance, strong reserves, and liquidity (including funds outside of the general fund),
- Strong financial management policies and practices, including high reserve policy and comprehensive capital planning,
- Affluent tax base supporting a strong, community funded status, that insulates district from enrollment declines,
- Long-standing revenue sharing agreement that leads to financial certainty.

Moody's

Rating Action: Moody's assigns Aaa to Fremont UHSD, CA's (Santa Clara County) GO Bonds (Election of 2018), Series 2023, GO Bonds (Election of 2022), Series 2023 and 2023 General Obligation Refunding Bonds; outlook is stable

24 Apr 2023
